

Woodburn Community Center

City Council Meeting 06.26.2023





Meeting Agenda

Welcome

Review Current Design

Site + Landscape

Building Layout

Architectural Character

Exterior Character

Interior Character

Project Cost Update


Project Schedule Update

Questions & Discussion



Woodburn

Context Plan

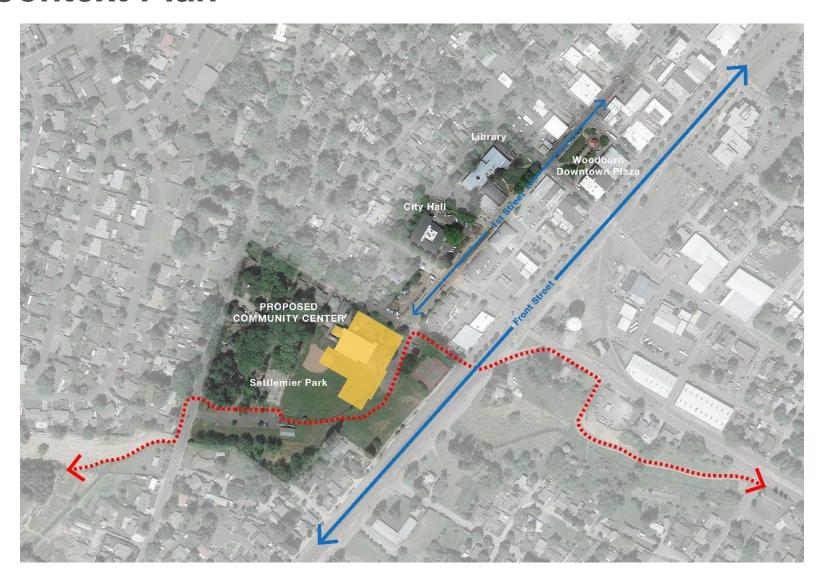

WOODBURN

Base Site Plan



Woodburn

Full Buildout Site Plan





View above Settlemier Park



Oak Street Entry Plaza & Character










PLAZA PLANTINGS



STORMWATER PLANTINGS



STORMWATER CHANNEL









- 1 Entry Lobby
- 2 Reception / Administrative
- 3 Community Multi-Purpose Room
- 4 Partner Office Suite
- 5 Locker Rooms
- 6 Existing Lap Pool
- 7 New Water Slide
- **New Warm Water Recreation Pool**
- 9 Gymnasium Two-Court Divisible








Full Buildout Plan - Level 2



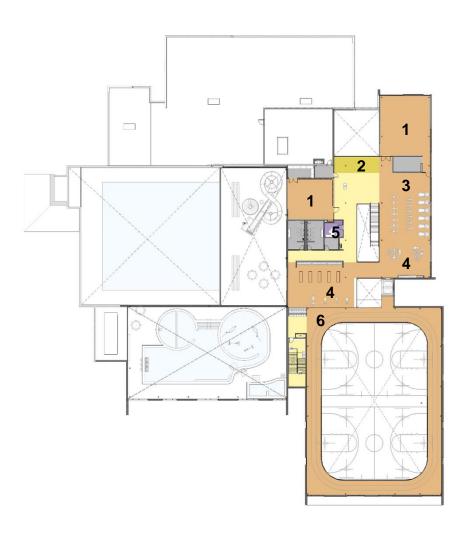

- 1 Multi Purpose Exercise
- 2 Stretching
- 3 Cardio
- 4 Weights
- **5** Fitness Assessment
- Elevated Walking & Jogging Track












- 1 Entry Lobby
- 2 Reception / Administrative
- 3 Community Multi-Purpose Room
- 4 Locker Rooms
- 5 Existing Lap Pool
- 6 Existing Wading Pool
- 7 Gymnasium One-Court Divisible








Base Plan - Level 2

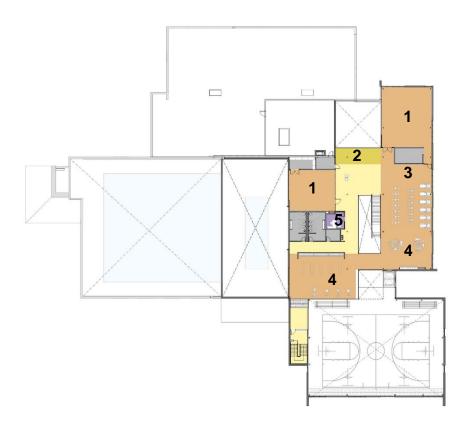

- 1 Multi Purpose Exercise
- 2 Stretching
- 3 Cardio
- 4 Weights







Site Context











Community & Culture











Approach from 1st St





East Entry Approach





View from Settlemier Park





Entry Lobby & Lounge





Multi-Use Gymnasium





Cardio-Weight Space





New Warm Water Recreation Pool





Capital & Operational Costs


Base Plan

SD 04.21.2023 - Update

	Nov 2025	Feb 2026
Direct Construction Cost	\$31.9 M	\$32.4 M
Indirect Project Cost	\$9.6 M	\$9.7 M
Total Capital Costs	\$41.5 M	\$42.1 M

NOT UPDATED


Expenses	\$1.6 - \$1.9 M
Revenues	\$0.9 - \$1.1 M
Operations Difference	(\$700 - 800 K)



Schematic Design 01.30.2020

	Aug 2022
Direct Construction Cost	\$25.2 M
Indirect Project Cost	\$7.6 M
Total Capital Costs	\$32.8 M

Expenses	\$1.6 - \$1.9 M
Revenues	\$0.9 - \$1.1 M
Operations Difference	(\$700 - 800 K)




Total Building Gross Area 55,335 GSF

Total Building Gross Area 55,335 GSF









Total Building Gross Area 75,980 GSF

SD 04.21.2023 - Update

Warm Water Pool Alternate

Nov 2025	Feb 2026
\$7.2 M	\$7.3 M
\$2.1 M	\$2.2 M
\$9.3 M	\$9.5 M
	\$7.2 M \$2.1 M

2nd Gymnasium Court Alternate

Direct Construction Cost	\$4.8 M	\$4.9 M
Indirect Project Cost	\$1.4 M	\$1.5 M
Total Capital Costs	\$6.2 M	\$6.4 M

Elevated Running Track Alternate

Direct Construction Cost	\$0.84 M	\$0.85 M
Indirect Project Cost	\$0.25 M	\$0.26
Total Capital Costs	\$1.09 M	\$1.11 M

Partner Office Suite Alternate

Direct Construction Cost	\$0.58 M	\$0.59 M
Indirect Project Cost	\$0.17 M	\$0.18 M
Total Capital Costs	\$0.75 M	\$0.77 M

Schematic Design

Warm Water Pool Alternate

	Aug 2022
Direct Construction Cost	\$5.6 M
Indirect Project Cost	\$1.6 M
Total Capital Costs	\$7.2 M

2nd Gymnasium Court Alternate

Direct Construction Cost	\$3.4 M
Indirect Project Cost	\$1.0 M
Total Capital Costs	\$4.4 M

Elevated Running Track Alternate

Direct Construction Cost	\$0.4 M
Indirect Project Cost	\$0.1 M
Total Capital Costs	\$0.5 M

Partner Office Suite Alternate

Direct Construction Cost	\$0.5 M
Indirect Project Cost	\$0.1 M
Total Capital Costs	\$0.6 M





Capital & Operational Costs


Base Plan + Alternates

SD 04.21.2023 - Update

	Nov 2025	Feb 2026
Direct Construction Cost	\$45.4 M	\$46.0 M
Indirect Project Cost	\$13.6 M	\$13.8 M
Total Capital Costs	\$59 M	\$59.8

NOT UPDATED

Expenses	\$1.81 - \$2.21 M
Revenues	\$1.30 - \$1.56 M
Operations Difference	(\$515 – 645 K)

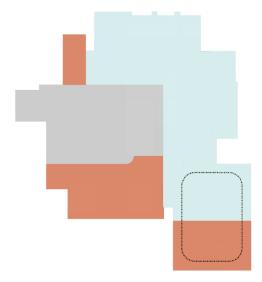


Total Building Gross Area 75,980 GSF

Schematic Design Phase

	Aug 2022
Direct Construction Cost	\$35.6 M
Indirect Project Cost	\$10.7 M
Total Capital Costs	\$46.3 M

Expenses	\$1.81 - \$2.21 M
Revenues	\$1.30 - \$1.56 M
Operations Difference	(\$515 – 645 K)

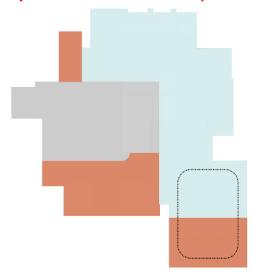

Total Building Gross Area 75,980 GSF





Capital Costs

Base Plan + Alternates + Site Alternates

SD 04.21.2023 - Update


Nov 2025	Feb 2026
\$45.4 M	\$46.0 M
\$13.6 M	\$13.8 M
\$59 M	\$59.8
	\$45.4 M \$13.6 M

Site Alternates

Direct Construction Cost	\$0.55 M	\$0.56 M
Indirect Project Cost	\$0.16 M	\$0.17 M
Operations Difference	\$0.71	\$0.73

All In Total \$59.7 M \$60.5 M



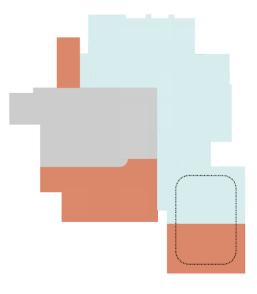

Total Building Gross Area 75,980 GSF



Development / Construction Schedule

November 2024 Bond In	itiative
-----------------------	----------

Project Item	Date
Bond Measure Election	November 2024
Design services contract executed	December 2024
Design Development	January 2025 - March 2025
Construction Documents	April 2025 - August 2025
Permitting	September 2025 - October 2025
Construction Start	November 2025
State funds would need to be spent by	April/May 2026

May	2025	Bond	Initiative

Project Item	Date
Design services contract executed	January 2025
Design Development	January 2025 - March 2025
Bond Measure Election	May 2025
Construction Documents	June 2025 – December 2025
Permitting	March 2026 - April 2026
Construction Start	May 2026
State funds would need to be spent by	April/May 2026

Additional Project Development Components



CITIZENS ADVISORY COMMITTEE (CAC):

- Establishing a new CAC by resolution (Summer 2023)
 - New resolution will include a provision terminating CAC prior to the bond measure language being submitted to Marion County Elections Official.
 - Nothing will prohibit members or former members of the CAC from forming a political action committee (PAC) or otherwise supporting or opposing a potential community center bond measure. *

*The City will not be able to support the PAC or be involved in these activities in any manner.



Additional Project Development Components (cont.)



Bond Measure Preparations

- Bond Measure Financial Analysis (Summer Fall 2023)
 - The City has engaged its financial advisor to perform a bond measure analysis, which will include a review of the preliminary bond size, levy rate, amortization period, interest rates, and the economic impact of the bonds. This work will include advice to staff and the City Council regarding the structure of the bond sale.
- Election Consultant (Fall 2023)
 - It is generally recommended that the City hire an elections consultant to provide strategic advice regarding the bond measure campaign, including a campaign assessment, measure design & messaging, public opinion research, and data modeling.



Additional Project Development Components (cont.)



Bond Measure Preparations (cont.)

- Update Operational Financial Analysis (Spring 2024)
 - Staff will work with the community center consultant team to update the operations and maintenance financial projects. The original analysis was performed in 2020 and has become somewhat outdated. Prior to making the decision to place the bond measure on the ballot, it is important for the City to have up to date operating cost/ revenue estimates.
- Fund Development Consultant (Fall 2023)
 - In order to reduce the size of the potential bond measure, the City may elect to hire a fund development consultant to conduct private fundraising activities.

Complete Project Timeline



November 2024 Bond Measure Election		
Project Item	Dates	
Reappoint Members to the Citizens Advisory Committee (CAC)	Summer 2023	
Conduct Bond Measure Financial Analysis	Summer 2023 – Fall 2023	
Fund Development Campaign	Fall 2023 – Fall 2024	
Hire Election Consultant	Fall 2023	
Conduct Registered Voter Polling	Winter 2023 – Spring 2024	
Update Operational Financial Analysis	Spring 2024	
Ballot Language Submitted to Marion County Elections Official	August 2024	
Bond Measure Election	November 2024	
Complete Architectural & Engineering Design Work	December 2024 - Fall 2025	
Community Center Construction	Fall 2025 – Fall 2027	
Community Center Opens to the Public	Fall 2027	



Complete Project Timeline



May 2025 Bond Measure Election		
Project Item	Dates	
Bond Measure Fails to Pass	November 2024	
Evaluate Election Results and Determine Whether or not to Place Project on May 2025 Ballot	November 2024 – December 2024	
Complete "Design Development" Phase of Architectural & Engineering Design Work	January 2025 – March 2025	
Ballot Language Submitted to Marion County Elections Official	February 2025	
Bond Measure Election	May 2025	
Complete "Construction Documents" Phase of Architectural & Engineering Design Work	June 2025 – December 2025	
Community Center Construction	Winter 2026 – Winter 2028	
Community Center Opens to the Public	Winter 2028	





Questions & Discussion

